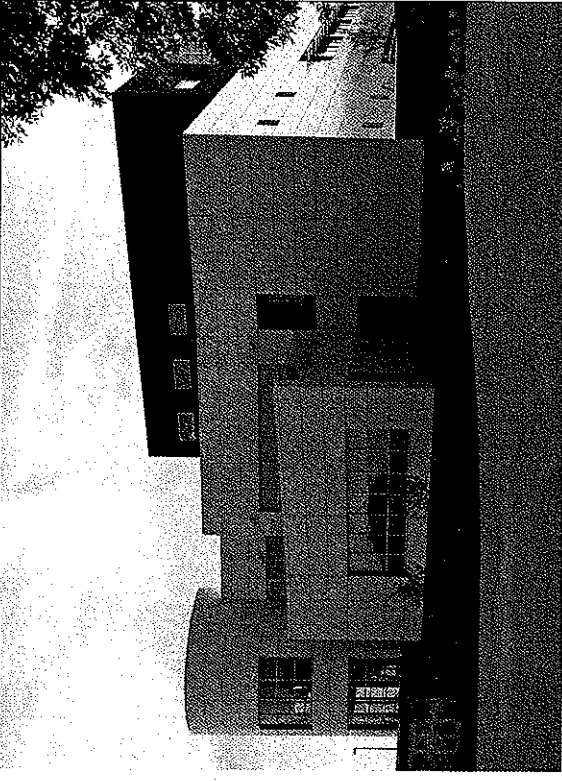

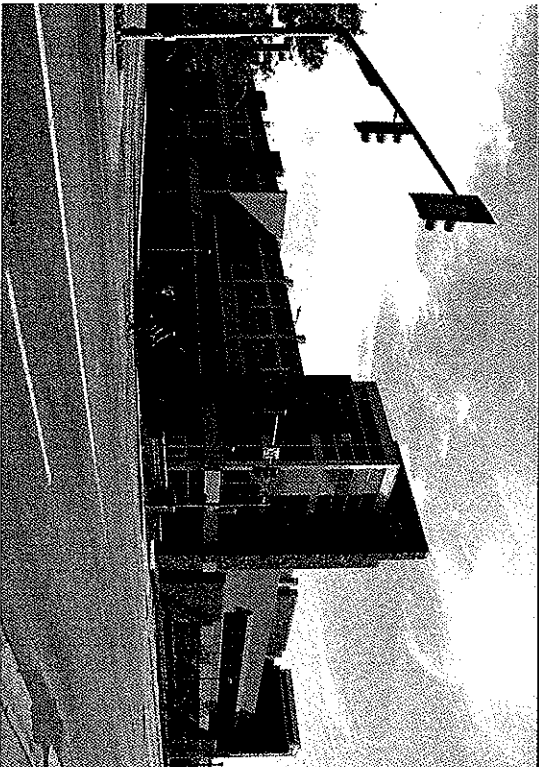
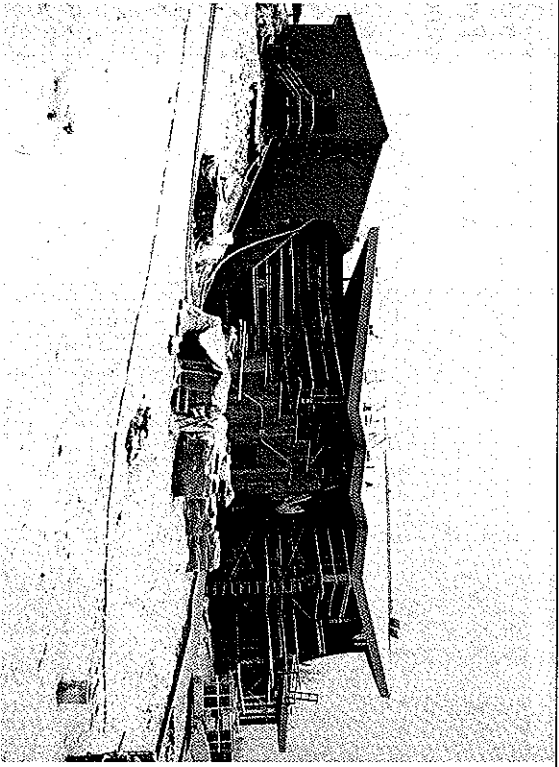
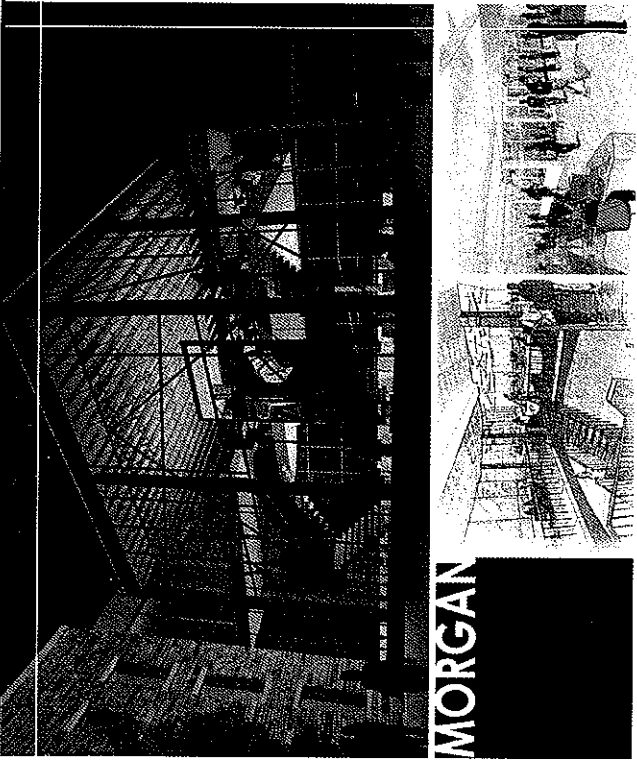

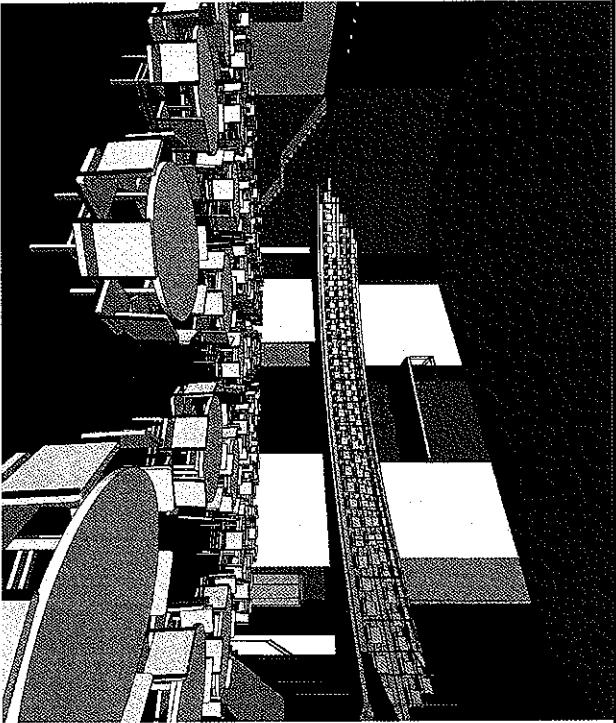
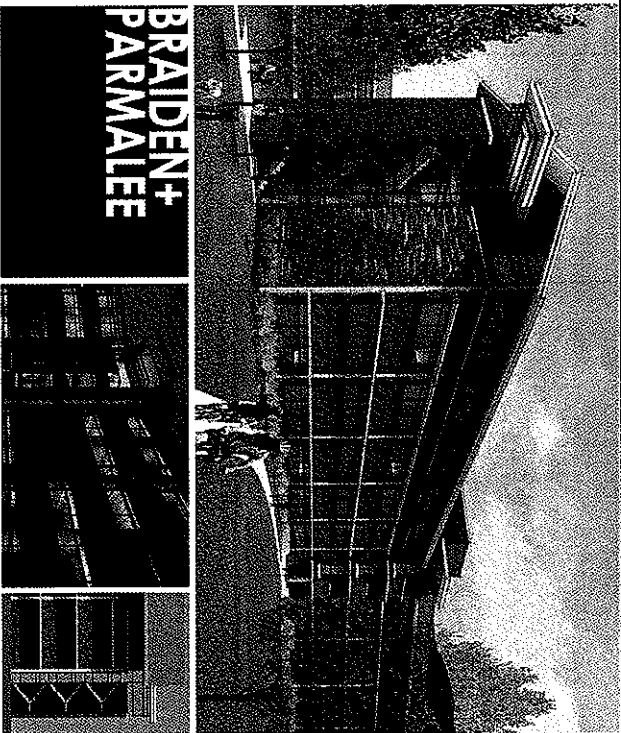



Project	Bond \$	Bond Project Status Picture	Occupancy	Status as of 11/10
Research Innovation Center Total Budget: \$52,000,000	\$52,000,000 CSU bonds		6/2010	RIC building is occupied. Guard house out to bid. Design of MRI suite in progress. Budget Status: In budget.
Student Recreation Center Total Budget: \$36,000,000	\$32,122,897 Rec Center Bonds		8/2010-Rec Center 4/2011-Pool	Rec Center is occupied, Pool renovation is underway. Budget Status: In budget.

Project	Bond \$	Bond Project Status Picture	Occupancy	Status as of 11/10
Lake Street Parking Garage Total Budget: \$21,600,000	\$21,600,000 Parking Fees		3/2010-parking	Occupied for parking in March 2010. Retail space and VTH tenant finish out for bid. Complete March 2011. Budget Status: In budget.
CIRA addition Total Budget: \$1,200,000	\$1,200,000 Research		1/11	Construction underway. Substantial completion in Jan 2011. Budget Status: In budget

Project	Bond \$	Bond Project Status Picture	Occupancy	Status as of 11/10
Morgan Library Expansion Total Budget: \$16,800,000	\$16,400,000 Student Facility Fee		June 2012	Project is in design.
Engineering II Total Budget: \$58,000,000	\$40,000,000 Student Facility Fee		March 2013	Project is in design.

Project	Bond \$	Bond Project Status Picture	Occupancy	Status as of 11/10
Lory Student Center Theater Renovation Total Budget: \$6,000,000	\$6,000,000 Student Center Fees		Aug 2012	Project is in design.
Braiden and Parmelee Halls 4 th floor addition Total Budget: \$26,000,000	\$26,000,000 Housing and Dining Services		Aug 2013	Project is in design.

Project	Bond \$	Bond Project Status Picture	Occupancy	Status as of 11/10
Classroom upgrades Total Budget: \$10,000,000	\$10,000,000 Student Facility Fee and General Fund	 <div style="display: flex; justify-content: space-around; margin-top: 10px;"> <div style="border: 1px solid black; padding: 5px;">Before</div> <div style="border: 1px solid black; padding: 5px;">After</div> </div>	Dec 2011	4 classrooms in Eddy Hall complete. New furniture ordered and in place in classrooms. Design work continuing.
